ID	Task Mode	Task Name	Duration	Start	Finish
1		Erect fence and site welfare units	1 day	22/06/15	22/06/15
2		Delivery of shoring equipment	1 day	23/06/15	23/06/15
3		Break Rock	2 days	23/06/15	24/06/15
4		Install frame	1 day	24/06/15	24/06/15
5		Install sheet piles	2 days	25/06/15	26/06/15
6		Excavate tank farm	2 days	26/06/15	29/06/15
7		Prepare and concrete base	1 day	30/06/15	30/06/15
8		Pea shingle base	1 day	01/07/15	01/07/15
9		Install tanks	0.5 days	02/07/15	02/07/15
10		Pea shingle surround to tanks	1.5 days	03/07/15	06/07/15
11		Extract shoring	1 day	06/07/15	06/07/15
12		Remove shoring from site	1 day	07/07/15	07/07/15
13		Install Forecourt interceptor	2 days	14/07/15	15/07/15
14		Set out, excavate, pour canopy pads	2 days	07/07/15	09/07/15
15		Install canopy stub columns	1 day	09/07/15	10/07/15
16		Install Pump cradles	1 day	10/07/15	13/07/15
17		BWIC Pipe work trenches	1 day	10/07/15	13/07/15
18		Install Tank internals	1 day	15/07/15	15/07/15
19		Install fuel suction lines	2 days	16/07/15	17/07/15
20		Install offset fill / vent lines	1 day	20/07/15	20/07/15
21		Test pipe work	1 day	21/07/15	21/07/15
22		Petroleum officer Inspection	1 day	21/07/15	21/07/15
23		Install below ground drainage	4 days	21/07/15	24/07/15
24		Install below ground service ducts	4 days	21/07/15	24/07/15
25		Backfill to pipe work	2 days	22/07/15	23/07/15
26		Backfill / capping to levels	2 days	24/07/15	27/07/15
27		Install new kerb lines	7 days	21/07/15	29/07/15
28		Concrete islands	2 days	30/07/15	31/07/15
29		Excavate and lay BT / Elec ducts/Water	10 days	17/07/15	30/07/15
30		Prep and concrete base to Control Unit	2 days	10/07/15	13/07/15
31		Install Control Unit housing	1 day	15/07/15	15/07/15
32		Screed to base of control unit	1 day	17/07/15	17/07/15
33		Pull in BT cable	1 day	20/07/15	20/07/15
34		Install BT DP terminal	1 day	21/07/15	21/07/15
35		BT ADSL Line Conversion	1 day	11/08/15	11/08/15
36		Lay Aco channels Prepare concrete	2 days	27/07/15	28/07/15
37		Lay concrete bays	5 days	24/07/15	30/07/15
38		Tarmac PFS forecourt	1 day	31/07/15	31/07/15
39		Tarmac to car park	2 days	03/08/15	04/08/15
40		Road markings	2 days	06/08/15	07/08/15
41		Erect Canopy	2 days	10/08/15	11/08/15
42		CCTV	2 days	11/08/15	12/08/15
43		Signage to canopy / site / Totem	1 day	14/08/15	14/08/15
44		Tank Gauges / DCD / Emergency box	2 days	03/08/15	04/08/15
45		Site electrics	16 days	27/07/15	17/08/15
46		Electrical connection	1 day	31/07/15	31/07/15
47		air / water unit	1 day	12/08/15	12/08/15
48		Grit bin	1 day	12/08/15	12/08/15
49		Fire equipment	1 day	12/08/15	12/08/15
50		Install Pumps	1 day	12/08/15	12/08/15
51		Wire pumps	1 day	12/08/15	12/08/15
52		Issue electrical cert	1 day	13/08/15	13/08/15
53		Issue ASDA check list (pm)	1 day	13/08/15	13/08/15
54		Petroleum officer Inspection (pm)	1 day	13/08/15	13/08/15
55		Splash load fuel delivery (AM delivery)	1 day	14/08/15	14/08/15
56		Commission pumps	1 day	14/08/15	14/08/15
57		Weights and measures	1 day	17/08/15	17/08/15
58		GVR Programme / Mapping	1 day	17/08/15	17/08/15
59		HTEC	3 days	13/08/15	17/08/15
60		Clean site	2 days	17/08/15	18/08/15
61		Handover to Asda	1 day	19/08/15	19/08/15
62		278 Works	10 days	29/06/15	10/07/15
63		BT chamber works	3 days	29/06/15	01/07/15
64		BT complete	1 day	10/07/15	10/07/15

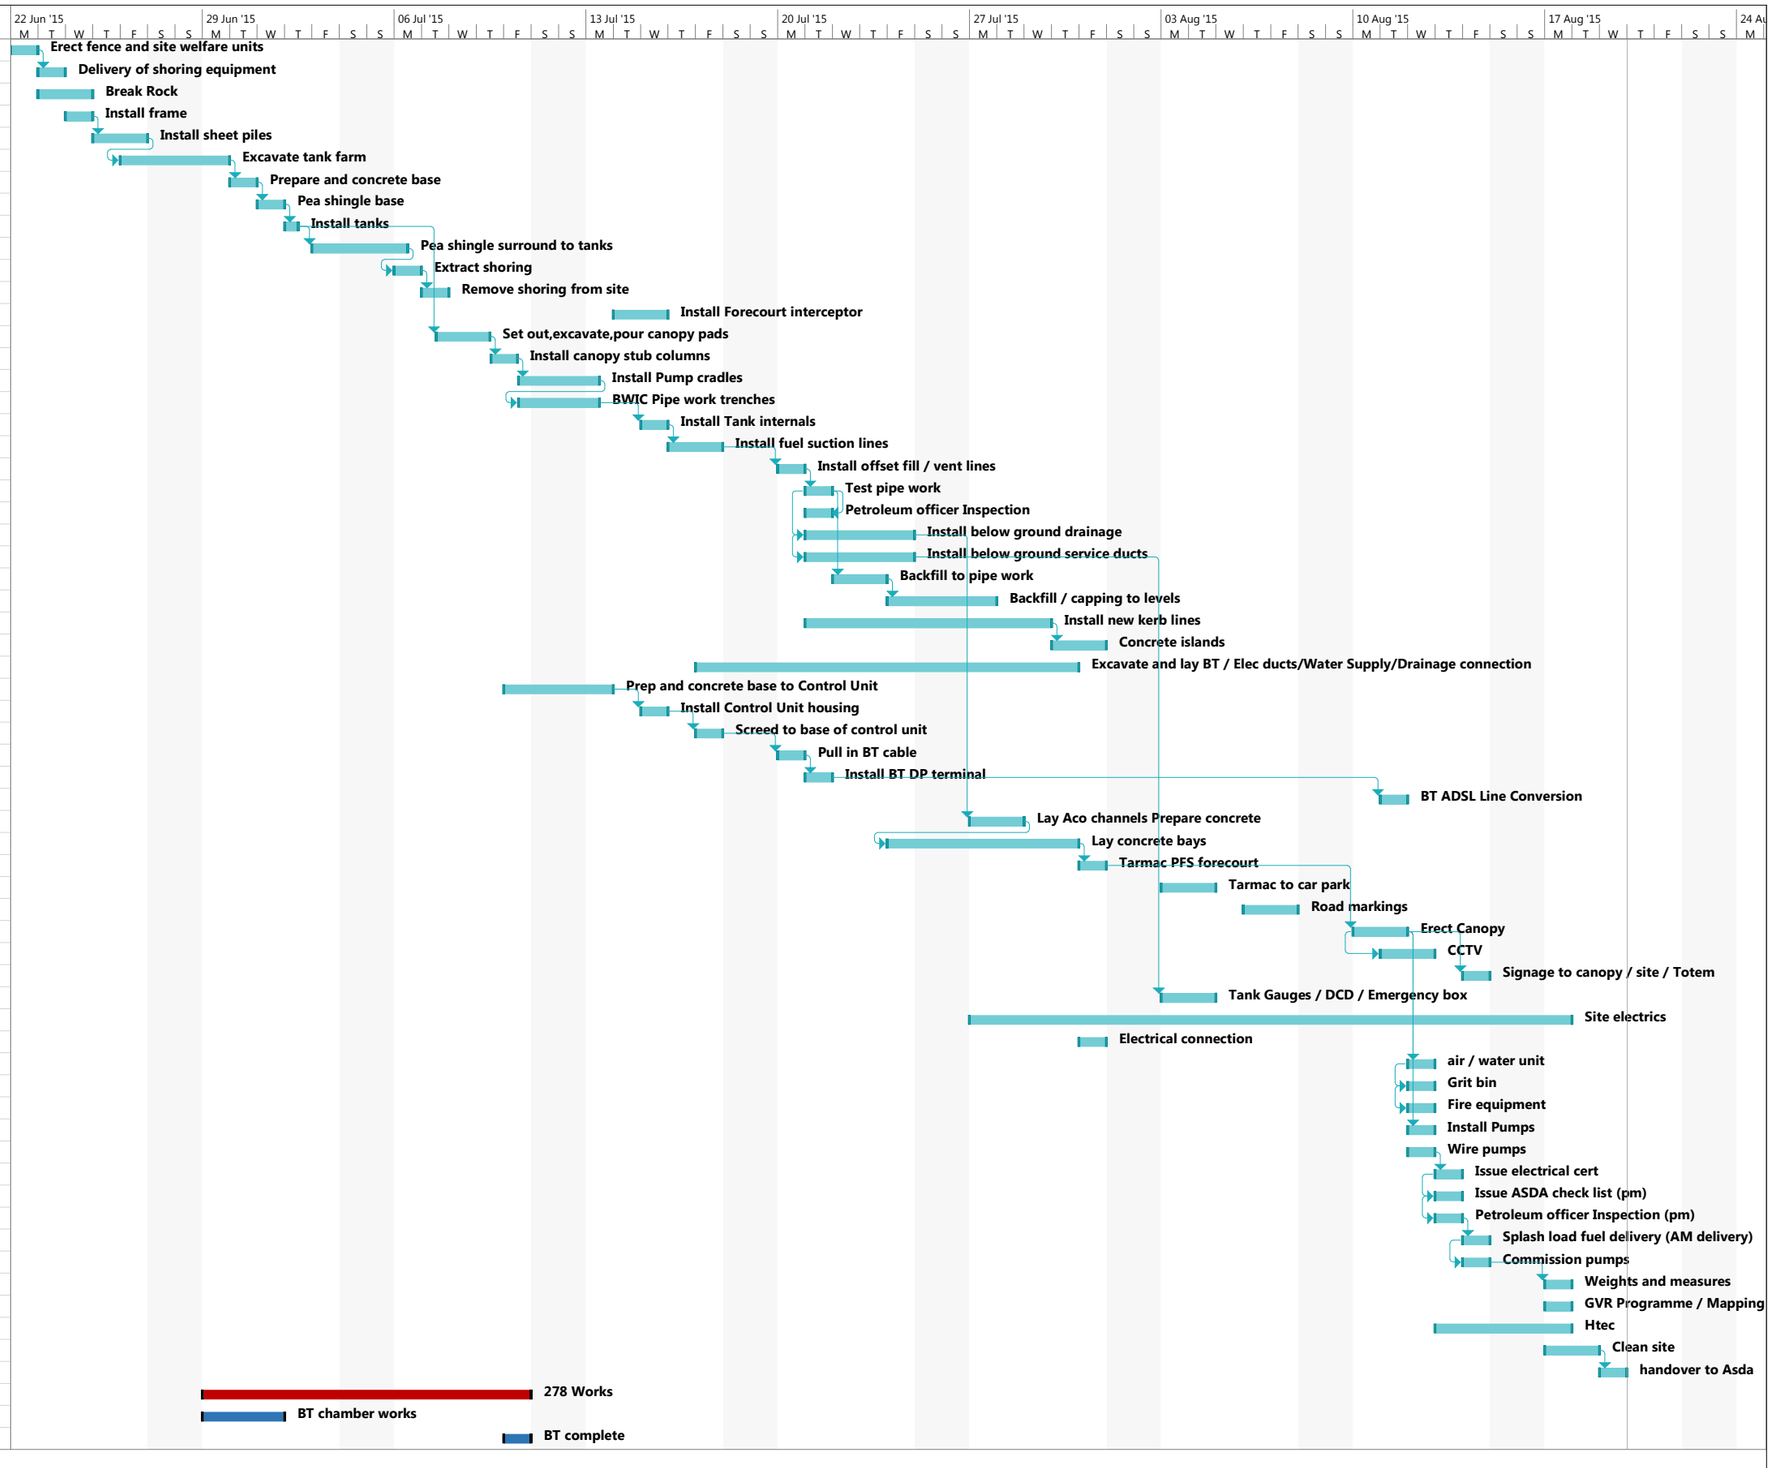

Project: Asda Breck Road
Date: 28/05/15

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
